





















PMBOK Guide - 4th Edition Schedule

ID		Task Name	Duration	% comp	Start	Finish	Predecessors
1		Initiation	85 days	100%	Wed 7/5/06	Thu 10/26/06	
16		Planning	96.25 days	100%	Mon 10/2/06	Mon 2/12/07	
35		Development	459.5 days	26%	Wed 11/1/06	Fri 8/1/08	
36		Open call for volunteers	0 days	100%	Fri 11/10/06	Fri 11/10/06	
37		On board volunteers	8 wks	100%	Fri 11/10/06	Thu 1/4/07	36
38		Mapping Change Request for Chapters 5-12	2 wks	100%	Mon 1/8/07	Fri 1/19/07	
39		Processes finalized	0 days	100%	Thu 2/1/07	Thu 2/1/07	38
40		Inputs and Outputs for existing processes final	0 days	100%	Thu 3/1/07	Thu 3/1/07	39FF+4 wks
41		Inputs and outputs for new processes final	0 days	100%	Fri 3/30/07	Fri 3/30/07	39
42		Develop ITTO Tables	4 wks	0%	Mon 5/21/07	Fri 6/15/07	
43		Chapter 1	131 days	67%	Wed 11/1/06	Mon 4/30/07	
44		Ch 1 Architecture complete	3 wks	100%	Wed 11/1/06	Tue 11/21/06	
45		Annotated Outline for Chapter 1	3 wks	100%	Wed 11/22/06	Tue 12/12/06	44
46		Ch 1 Draft 1	8 wks	100%	Thu 2/1/07	Mon 3/26/07	45
47		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/7/07	Wed 3/7/07	
48		Team and Q/I review	2 wks	0%	Tue 3/27/07	Mon 4/9/07	46
49		Compile comments	2 wks	0%	Tue 4/10/07	Mon 4/23/07	48
50		Develop Figures and Models	2 wks	0%	Tue 4/10/07	Mon 4/23/07	49FF
51		Baseline Chapter 1 1.0	0 days	0%	Mon 4/23/07	Mon 4/23/07	49
52		Editorial Review 1.1	1 wk	0%	Tue 4/24/07	Mon 4/30/07	51
53		Chapter 2	126 days	59%	Wed 11/22/06	Mon 5/14/07	
54		Ch 2 Architecture complete	3 wks	100%	Wed 11/22/06	Tue 12/12/06	44
55		Annotated Outline for Chapter 2	3 wks	100%	Wed 12/13/06	Tue 1/2/07	54
56		Ch 2 Draft 1	10 wks	75%	Thu 2/1/07	Mon 4/9/07	55
57		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/14/07	Wed 3/14/07	
58		Team and Q/I Review	2 wks	0%	Tue 4/10/07	Mon 4/23/07	56
59		Compile comments	2 wks	0%	Tue 4/24/07	Mon 5/7/07	58
60		Develop Figures and Models	2 wks	0%	Tue 4/24/07	Mon 5/7/07	59FF
61		Baseline Chapter 2 1.0	0 days	0%	Mon 5/7/07	Mon 5/7/07	60
62		Editorial Review 1.1	1 wk	0%	Tue 5/8/07	Mon 5/14/07	61
63		Chapter 3	168 days	55%	Wed 12/13/06	Wed 8/1/07	
64		Ch 3 Architecture complete	3 wks	100%	Wed 12/13/06	Tue 1/2/07	54
65		Annotated Outline for Chapter 3	2 wks	100%	Thu 1/25/07	Wed 2/7/07	64

PMBOK Guide - 4th Edition Schedule

ID		Task Name	Duration	% comp	Start	Finish	Predecessors
66		Write process descriptions	8 wks	100%	Thu 2/8/07	Mon 4/2/07	65
67		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/21/07	Wed 3/21/07	
68		Ch 3 Draft 1	18 wks	50%	Mon 2/26/07	Wed 6/27/07	94FF
69		Develop Figures	4 wks	0%	Thu 5/31/07	Wed 6/27/07	68FF
70		Team and Q/I Review	2 wks	0%	Thu 6/28/07	Wed 7/11/07	69
71		Compile comments	2 wks	0%	Thu 7/12/07	Wed 7/25/07	70
72		Baseline Chapter 3 1.0	0 days	0%	Wed 7/25/07	Wed 7/25/07	71
73		Editorial Review 1.1	1 wk	0%	Thu 7/26/07	Wed 8/1/07	72
74		Chapter 4	70 days	1%	Mon 3/26/07	Fri 6/29/07	
75		Ch 4 Draft 1	9 wks	0%	Mon 3/26/07	Fri 5/25/07	
76		Develop Figures	4 wks	0%	Mon 4/30/07	Fri 5/25/07	75FF
77		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/28/07	Wed 3/28/07	
78		Team and Q/I Review	2 wks	0%	Mon 5/28/07	Fri 6/8/07	75
79		Compile Comments	2 wks	0%	Mon 6/11/07	Fri 6/22/07	78
80		Baseline Chapter 4 1.0	0 days	0%	Fri 6/22/07	Fri 6/22/07	79
81		Editorial Review 1.1	1 wk	0%	Mon 6/25/07	Fri 6/29/07	80
82		Chapter 5	119 days	17%	Thu 2/1/07	Fri 7/13/07	
83		Ch 5 Draft 1	18.6 wks	25%	Thu 2/1/07	Thu 6/7/07	
84		Develop Figures	4 wks	0%	Fri 5/11/07	Thu 6/7/07	83FF
85		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/28/07	Wed 3/28/07	
86		Team and Q/I Review	2 wks	0%	Fri 6/8/07	Thu 6/21/07	83
87		Compile comments	2 wks	0%	Mon 6/25/07	Fri 7/6/07	86
88		Baseline Chapter 5 1.0	0 days	0%	Mon 7/9/07	Mon 7/9/07	87
89		Editorial Review 1.1	1 wk	0%	Mon 7/9/07	Fri 7/13/07	88
90		Chapter 6	124 days	18%	Thu 2/1/07	Fri 7/20/07	
91		Ch 6 Draft 1	19 wks	25%	Thu 2/1/07	Mon 6/11/07	
92		Develop Figures	2 wks	0%	Tue 5/29/07	Mon 6/11/07	91FF
93		QI Review 1 - 3rd Edition	1 day	0%	Wed 3/28/07	Wed 3/28/07	
94		Team and Q/I Review	2 wks	0%	Mon 6/18/07	Fri 6/29/07	91
95		Compile comments	2 wks	0%	Mon 7/2/07	Fri 7/13/07	94
96		Baseline Chapter 6 1.0	0 days	0%	Sun 7/15/07	Sun 7/15/07	95
97		Editorial Review 1.1	1 wk	0%	Mon 7/16/07	Fri 7/20/07	96
98		Chapter 7	64 days	51%	Thu 2/1/07	Fri 4/27/07	




















PMBOK Guide - 4th Edition Schedule

ID		Task Name	Duration	% comp	Start	Finish	Predecessors
99		Ch 7 Draft 1	3 wks	100%	Thu 2/1/07	Wed 2/21/07	
100		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/28/07	Wed 3/28/07	
101		Ch 7 Team Review	1 wk	100%	Thu 2/22/07	Wed 2/28/07	99
102		Compile comments	2 days	100%	Thu 3/1/07	Fri 3/2/07	101
103		Editorial review	5 days	100%	Mon 3/5/07	Fri 3/9/07	102
104		PMI Editor Review	2 days	100%	Mon 3/12/07	Tue 3/13/07	103
105		Q/I Review	1 day	100%	Sat 3/17/07	Sat 3/17/07	104
106		Q/I Edit	1 wk	100%	Mon 3/19/07	Fri 3/23/07	105
107		Develop Figures	3 wks	0%	Mon 3/19/07	Fri 4/6/07	105
108		Team Review	2 wks	0%	Mon 4/2/07	Fri 4/13/07	188,106
109		Compile comments	1 wk	0%	Mon 4/16/07	Fri 4/20/07	108
110		Baseline Chapter 7 1.0	0 days	0%	Fri 4/20/07	Fri 4/20/07	109,107
111		Final Editorial review 1.1	1 wk	0%	Mon 4/23/07	Fri 4/27/07	110
112		Chapter 8	103 days	1%	Thu 2/1/07	Thu 6/21/07	
113		Ch 8 Draft 1	15 wks	0%	Thu 2/1/07	Mon 5/14/07	
114		Develop Figures	2 wks	0%	Tue 5/1/07	Mon 5/14/07	113FF
115		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/28/07	Wed 3/28/07	
116		Team and QI Review	2 wks	0%	Tue 5/15/07	Mon 5/28/07	113
117		Compile Comments	2 wks	0%	Fri 6/1/07	Thu 6/14/07	116
118		Baseline Chapter 8 1.0	0 days	0%	Fri 6/15/07	Fri 6/15/07	117
119		Editorial review 1.1	1 wk	0%	Fri 6/15/07	Thu 6/21/07	118
120		Chapter 9	116 days	18%	Tue 2/6/07	Fri 7/13/07	
121		Ch 9 Draft 1	17 wks	25%	Tue 2/6/07	Thu 5/31/07	
122		Develop Figures	2 wks	0%	Fri 5/18/07	Thu 5/31/07	121FF
123		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/28/07	Wed 3/28/07	
124		Team and QI Review	2 wks	0%	Fri 6/1/07	Thu 6/14/07	121
125		Compile Comments	3 wks	0%	Fri 6/15/07	Thu 7/5/07	124
126		Baseline Chapter 9 1.0	0 days	0%	Mon 7/9/07	Mon 7/9/07	125
127		Editorial review 1.1	1 wk	0%	Mon 7/9/07	Fri 7/13/07	126
128		Chapter 10	116 days	1%	Tue 2/6/07	Fri 7/13/07	
129		Ch 10 Draft 1	19 wks	0%	Tue 2/6/07	Thu 6/14/07	
130		Develop Figures	2 wks	0%	Fri 6/1/07	Thu 6/14/07	129FF
131		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/28/07	Wed 3/28/07	

PMBOK Guide - 4th Edition Schedule

ID		Task Name	Duration	% comp	Start	Finish	Predecessors
132		Team and QI Review	1 wk	0%	Fri 6/15/07	Thu 6/21/07	129
133		Compile Comments	2 wks	0%	Fri 6/22/07	Thu 7/5/07	132
134		Baseline Chapter 10 1.0	0 days	0%	Fri 7/6/07	Fri 7/6/07	133
135		Editorial review 1.1	1 wk	0%	Mon 7/9/07	Fri 7/13/07	134
136		Chapter 11	115 days	4%	Wed 1/31/07	Fri 7/6/07	
137		Ch 11 Draft 1	18 wks	0%	Wed 1/31/07	Fri 6/1/07	
138		Develop Figures	2 wks	0%	Mon 5/21/07	Fri 6/1/07	137FF
139		QI Review 1 - 3rd Edition	5 days	100%	Wed 3/28/07	Tue 4/3/07	
140		Team and QI Review	2 wks	0%	Mon 6/4/07	Fri 6/15/07	137
141		Compile Comments	2 wks	0%	Mon 6/18/07	Fri 6/29/07	140
142		Baseline Chapter 11 1.0	0 days	0%	Fri 6/29/07	Fri 6/29/07	141
143		Editorial review 1.1	1 wk	0%	Mon 7/2/07	Fri 7/6/07	142
144		Chapter 12	90 days	1%	Wed 1/17/07	Fri 5/18/07	
145		Ch 12 Draft 1	13 wks	0%	Wed 1/17/07	Fri 4/13/07	
146		Develop Figures	1 wk	0%	Mon 4/9/07	Fri 4/13/07	145FF
147		QI Review 1 - 3rd Edition	1 day	100%	Wed 3/28/07	Wed 3/28/07	
148		Team and QI Review	2 wks	0%	Mon 4/16/07	Fri 4/27/07	145
149		Compile Comments	2 wks	0%	Mon 4/30/07	Fri 5/11/07	148
150		Baseline Chapter 12 1.0	0 days	0%	Fri 5/11/07	Fri 5/11/07	149
151		Editorial review 1.1	1 wk	0%	Mon 5/14/07	Fri 5/18/07	150
152		Integrated Content Reviews	34 days	0%	Fri 8/3/07	Wed 9/19/07	
153		Internal Team review	2 wks	0%	Fri 8/3/07	Thu 8/16/07	
154		Quality, Integration, Edit walk through	1 wk	0%	Fri 8/17/07	Thu 8/23/07	153
155		Edit based on team and walkthrough review	1 wk	0%	Fri 8/24/07	Thu 8/30/07	154
156		Librarian review	3 days	0%	Fri 8/31/07	Tue 9/4/07	155
157		Development buffer	2 wks	0%	Wed 9/5/07	Tue 9/18/07	156
158		Content Baselined	0 days	0%	Wed 9/19/07	Wed 9/19/07	157FF
159		Front and Back Material	376.5 days	4%	Mon 2/26/07	Fri 8/1/08	
160		Glossary changes due	0 days	0%	Sun 4/1/07	Sun 4/1/07	
161		Submit Glossary changes to LCB	9.6 wks	10%	Mon 2/26/07	Mon 4/30/07	
162		Revise glossary per Lexicon	3 wks	0%	Tue 9/4/07	Mon 9/24/07	
163		Review and proof glossary	2 wks	0%	Tue 9/25/07	Mon 10/8/07	162
164		Baseline glossary 1.0	0 days	0%	Mon 10/8/07	Mon 10/8/07	163


PMBOK Guide - 4th Edition Schedule

ID		Task Name	Duration	% comp	Start	Finish	Predecessors
165		Define appendices	1 wk	100%	Mon 3/12/07	Fri 3/16/07	
166		Define front material	1 wk	100%	Mon 3/12/07	Fri 3/16/07	
167		Develop appendices	40 days	0%	Fri 5/23/08	Fri 7/18/08	165
168		Appendix A - Fourth Edition Changes	8 wks	0%	Fri 5/23/08	Fri 7/18/08	209FF
169		Appendix B - Evolution	8 wks	0%	Fri 5/23/08	Fri 7/18/08	209FF
170		Appendix C - Contributors and Reviewers	8 wks	0%	Fri 5/23/08	Fri 7/18/08	209FF
171		Appendix E - Additional Sources of Information	8 wks	0%	Fri 5/23/08	Fri 7/18/08	209FF
172		Appendix F - Summary of PM Knowledge Area:	8 wks	0%	Fri 5/23/08	Fri 7/18/08	209FF
173		References	8 wks	0%	Fri 5/23/08	Fri 7/18/08	209FF
174		Develop front material	10 days	0%	Fri 7/4/08	Fri 7/18/08	166
175		TOC	2 wks	0%	Fri 7/4/08	Fri 7/18/08	209FF
176		List of Tables and Figures	2 wks	0%	Fri 7/4/08	Fri 7/18/08	209FF
177		Preface	2 wks	0%	Fri 7/4/08	Fri 7/18/08	209FF
178		Quality check	2 wks	0%	Fri 7/18/08	Fri 8/1/08	164,167,177
179		Baseline appendices 1.0	0 days	0%	Fri 8/1/08	Fri 8/1/08	178,164
180		Baseline front material 1.0	0 days	0%	Fri 8/1/08	Fri 8/1/08	178
181		PM work	200 days	32%	Mon 1/1/07	Wed 10/3/07	
182		Chapter Coordination	37.6 wks	50%	Mon 1/1/07	Mon 9/17/07	
183		SOWS - Budapest	2 days	0%	Mon 5/14/07	Tue 5/15/07	
184		PM/DPM Meeting	1.5 days	100%	Thu 2/22/07	Fri 2/23/07	
185		Dallas Team Meeting	2 days	100%	Fri 3/16/07	Sat 3/17/07	
186		Denver Team Meeting	2 days	0%	Fri 8/3/07	Mon 8/6/07	
187		Set up Content Review Mail Box	2 wks	100%	Mon 3/19/07	Fri 3/30/07	185
188		Set up content review process	2 wks	100%	Mon 3/19/07	Fri 3/30/07	185
189		Status reports	37.6 wks	30%	Wed 1/3/07	Wed 9/19/07	
190		Newsletters	28.8 wks	20%	Thu 3/1/07	Fri 9/14/07	
191		Change Control	33 wks	20%	Thu 2/1/07	Mon 9/17/07	
192		Issue, risk, assumption management	38 wks	30%	Mon 1/1/07	Wed 9/19/07	
193		Lessons learned	2 wks	0%	Thu 9/20/07	Wed 10/3/07	
194		Exposure	257.5 days	0%	Wed 9/19/07	Fri 9/12/08	157
195		<i>Q-SME, MAG and 5 project Integrator review</i>	2 wks	0%	Wed 9/19/07	Tue 10/2/07	
196		After MAG/SME/Integrator Edit	5 edays	0%	Tue 10/2/07	Sun 10/7/07	195
197		Quality walk through	2 edays	0%	Fri 10/5/07	Sun 10/7/07	196FF


PMBOK Guide - 4th Edition Schedule

ID	Task Name	Duration	% comp	Start	Finish	Predecessors
198	Librarian review	1 day	0%	Fri 10/5/07	Sun 10/7/07	197FF
199	PMI Editor does final edit	3 wks	0%	Mon 10/8/07	Fri 10/26/07	198
200	Q-ED posting	2 wks	0%	Mon 10/29/07	Fri 11/9/07	199
201	ED reviewed	60 days	0%	Mon 11/12/07	Fri 2/1/08	200
202	Review ED comments	3.5 wks	0%	Mon 2/4/08	Wed 2/27/08	201
203	Q-Comment Adjudication	6 wks	0%	Wed 2/27/08	Wed 4/9/08	202
204	Quality walk through	2 wks	0%	Wed 4/9/08	Wed 4/23/08	203
205	Edit based on team and Quality review	1 wk	0%	Wed 4/23/08	Wed 4/30/08	204
206	Librarian review	2 days	0%	Wed 4/30/08	Fri 5/2/08	205
207	Q-PMI Standards reviews Adjudicated Draft	3 wks	0%	Fri 5/2/08	Fri 5/23/08	206
208	Q-Appeals body processes adjudicated draft	5 wks	0%	Fri 5/23/08	Fri 6/27/08	207
209	Final edit	3 wks	0%	Fri 6/27/08	Fri 7/18/08	208
210	Q-Consensus Body	4 wks	0%	Fri 7/18/08	Fri 8/15/08	209
211	CEO approval	2 wks	0%	Fri 8/15/08	Fri 8/29/08	210
212	Exposure buffer	2 wks	0%	Fri 8/29/08	Fri 9/12/08	211
213	Print	60 days	0%	Fri 9/12/08	Fri 12/5/08	
214	Prep for printing	6 wks	0%	Fri 9/12/08	Fri 10/24/08	212
215	Print	4 wks	0%	Fri 10/24/08	Fri 11/21/08	214
216	Print buffer	2 wks	0%	Fri 11/21/08	Fri 12/5/08	215
217	Project close out	4 wks	0%	Fri 9/12/08	Fri 10/10/08	212


PMBOK Guide - 4th Edition Schedule

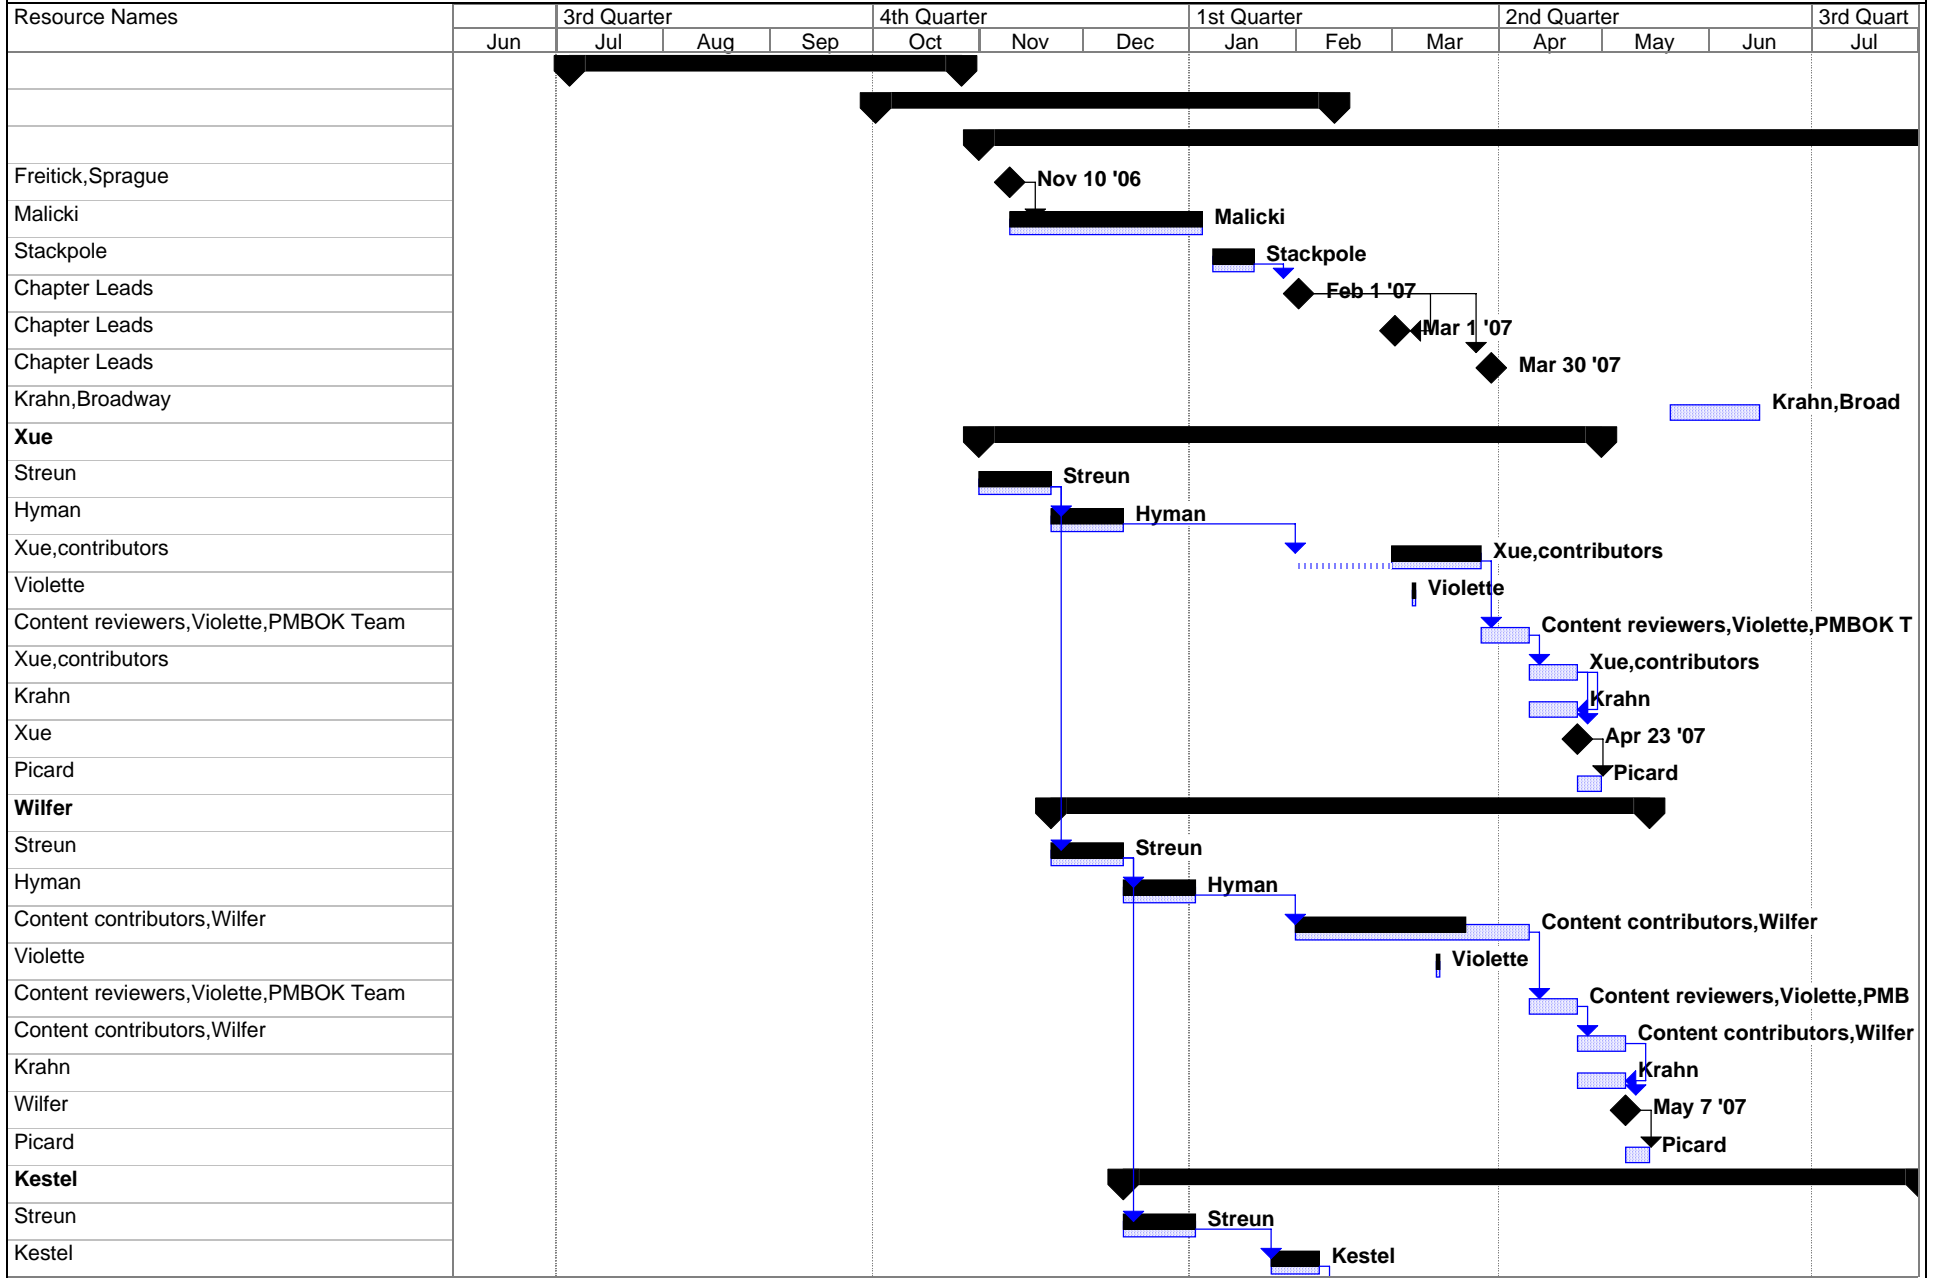


PMBOK Guide - 4th Edition Schedule

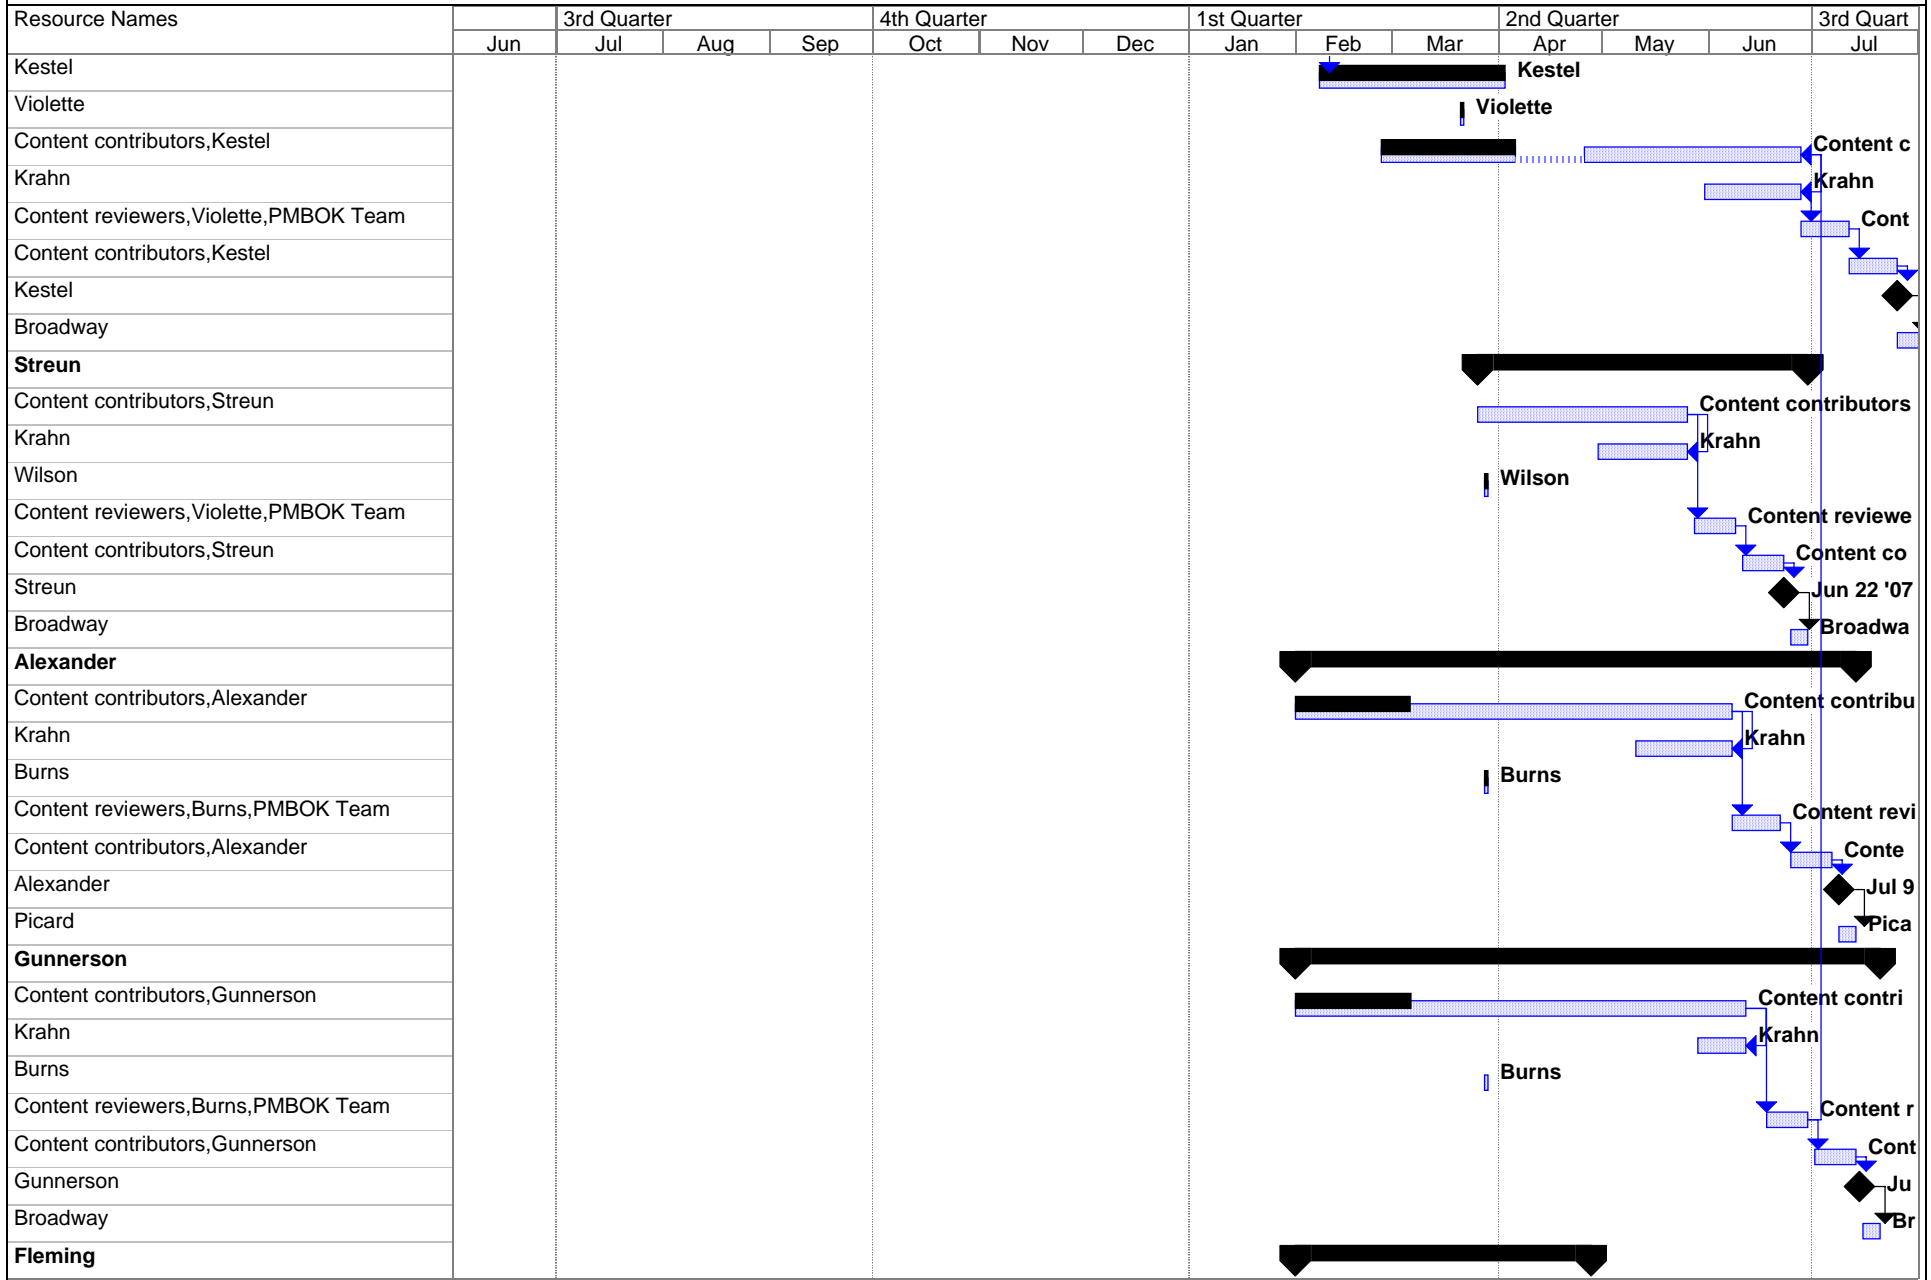

PMBOK Guide - 4th Edition Schedule

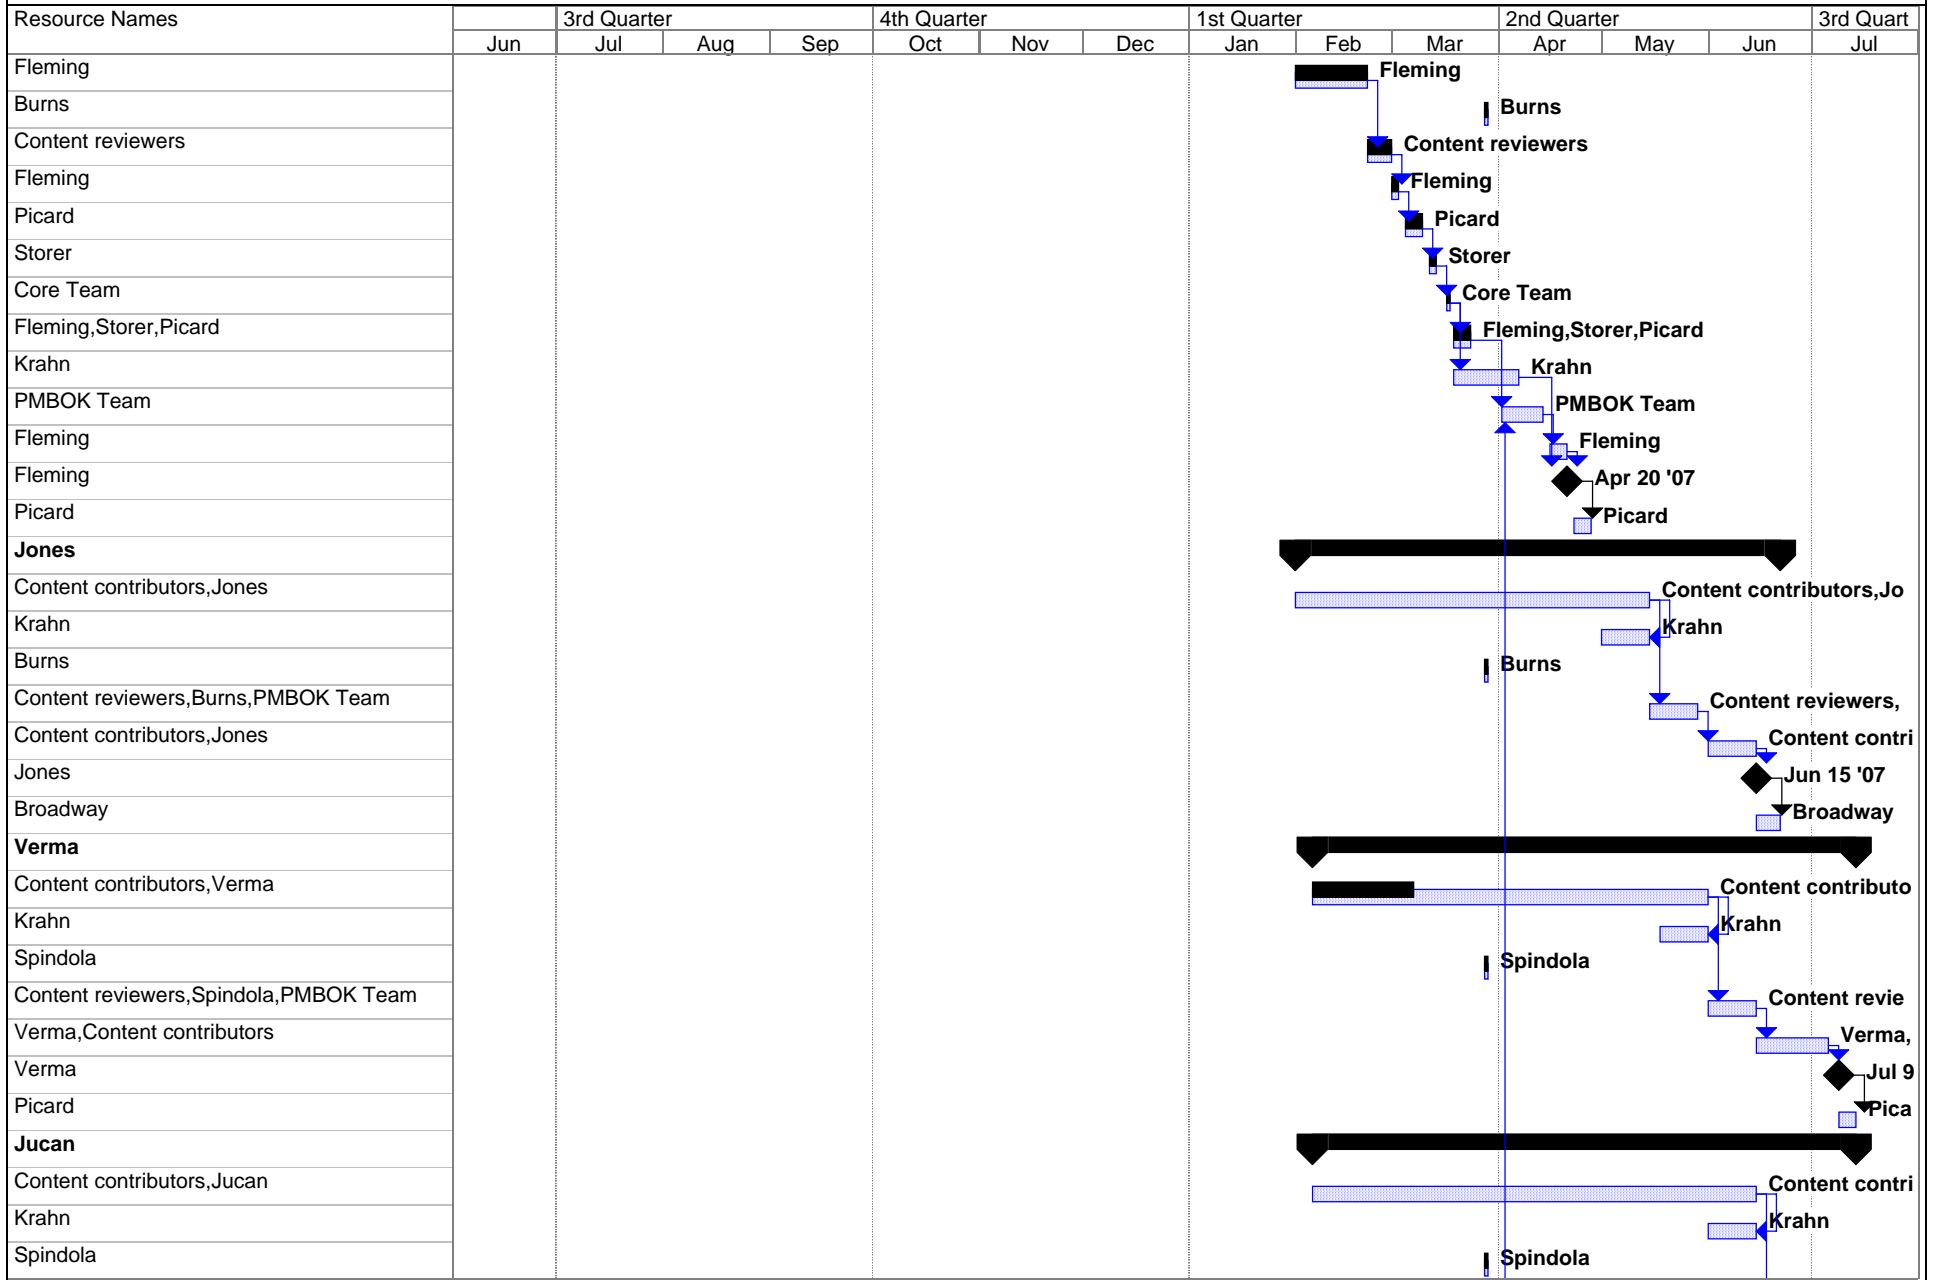

PMBOK Guide - 4th Edition Schedule

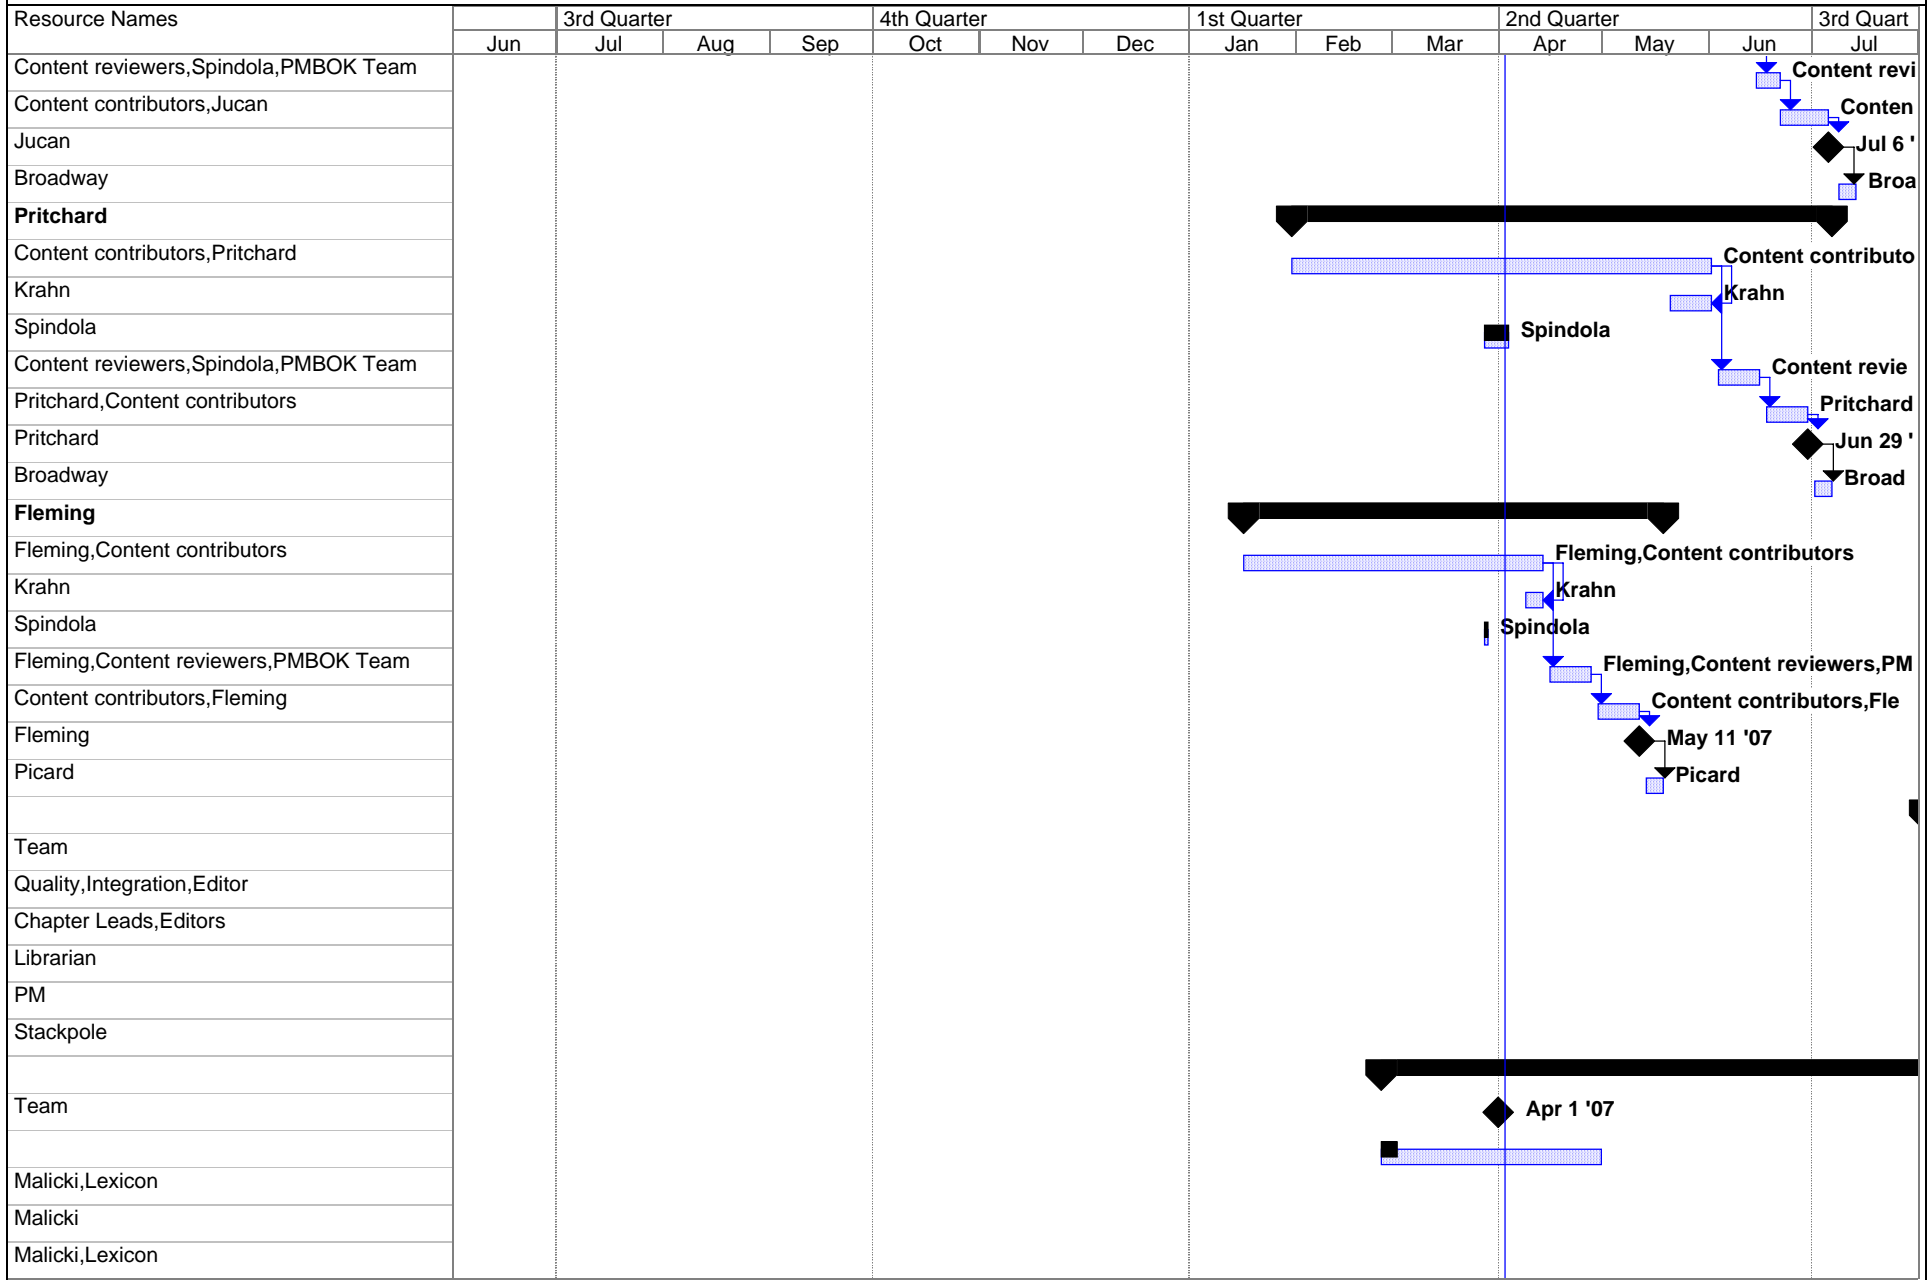

PMBOK Guide - 4th Edition Schedule

Resource Names	3rd Quarter				4th Quarter			1st Quarter			2nd Quarter			3rd Quart
	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
Malicki														
Malicki														
Malicki														
Malicki														
Malicki														
Malicki														
Malicki														
Malicki														
Malicki														
Malicki														
Malicki														
Stackpole														
Quality Lead														
Malicki														
Malicki														
Hyman,Stackpole,Rasmussen														
Stackpole,Dullnig														
Stackpole,Dullnig														
Team														
Team														
Vitello														
Jones,Kestel														
Team														
Grooms														
Stackpole														
Stackpole														
Grooms														
<i>MAG,SMEs,biehl</i>														
Editor														
Quality,Integration,Editor														

PMBOK Guide - 4th Edition Schedule

Resource Names	3rd Quarter				4th Quarter			1st Quarter			2nd Quarter			3rd Quart
	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
Librarian														
Storer														
<i>Kristin</i>														
<i>World</i>														
<i>Team</i>														
<i>Team</i>														
Quality,Integration,Editor														
Editor														
Librarian														
<i>Standards</i>														
<i>Team</i>														
<i>Editor</i>														
<i>Consensus Body</i>														
<i>Greg B</i>														
PM														
Barbara W														
Printer														

PMBOK Guide - 4th Edition Schedule

r	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quart		
	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
ay																		
eam																		
OK Team																		
r																		


PMBOK Guide - 4th Edition Schedule

r		4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quart
Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
<p>Contributors, Kestel</p> <p>Content reviewers, Violette, PMBOK Team</p> <p>Content contributors, Kestel</p> <p>Jul 25 '07</p> <p>Broadway</p> <p>, Streun</p> <p>rs, Violette, PMBOK Team</p> <p>Contributors, Streun</p> <p>y</p> <p>tors, Alexander</p> <p>iewers, Burns, PMBOK Team</p> <p>t contributors, Alexander</p> <p>'07</p> <p>rd</p> <p>utors, Gunnerson</p> <p>reviewers, Burns, PMBOK Team</p> <p>Content contributors, Gunnerson</p> <p>15 '07</p> <p>roadway</p>																	


PMBOK Guide - 4th Edition Schedule

r		4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quart
Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
<p>nes</p> <p>urns, PMBOK Team</p> <p>ibutors, Jones</p> <p>rs, Verma</p> <p>ers, Spindola, PMBOK Team</p> <p>Content contributors</p> <p>'07</p> <p>rd</p> <p>ibutors, Jucan</p>																	

PMBOK Guide - 4th Edition Schedule

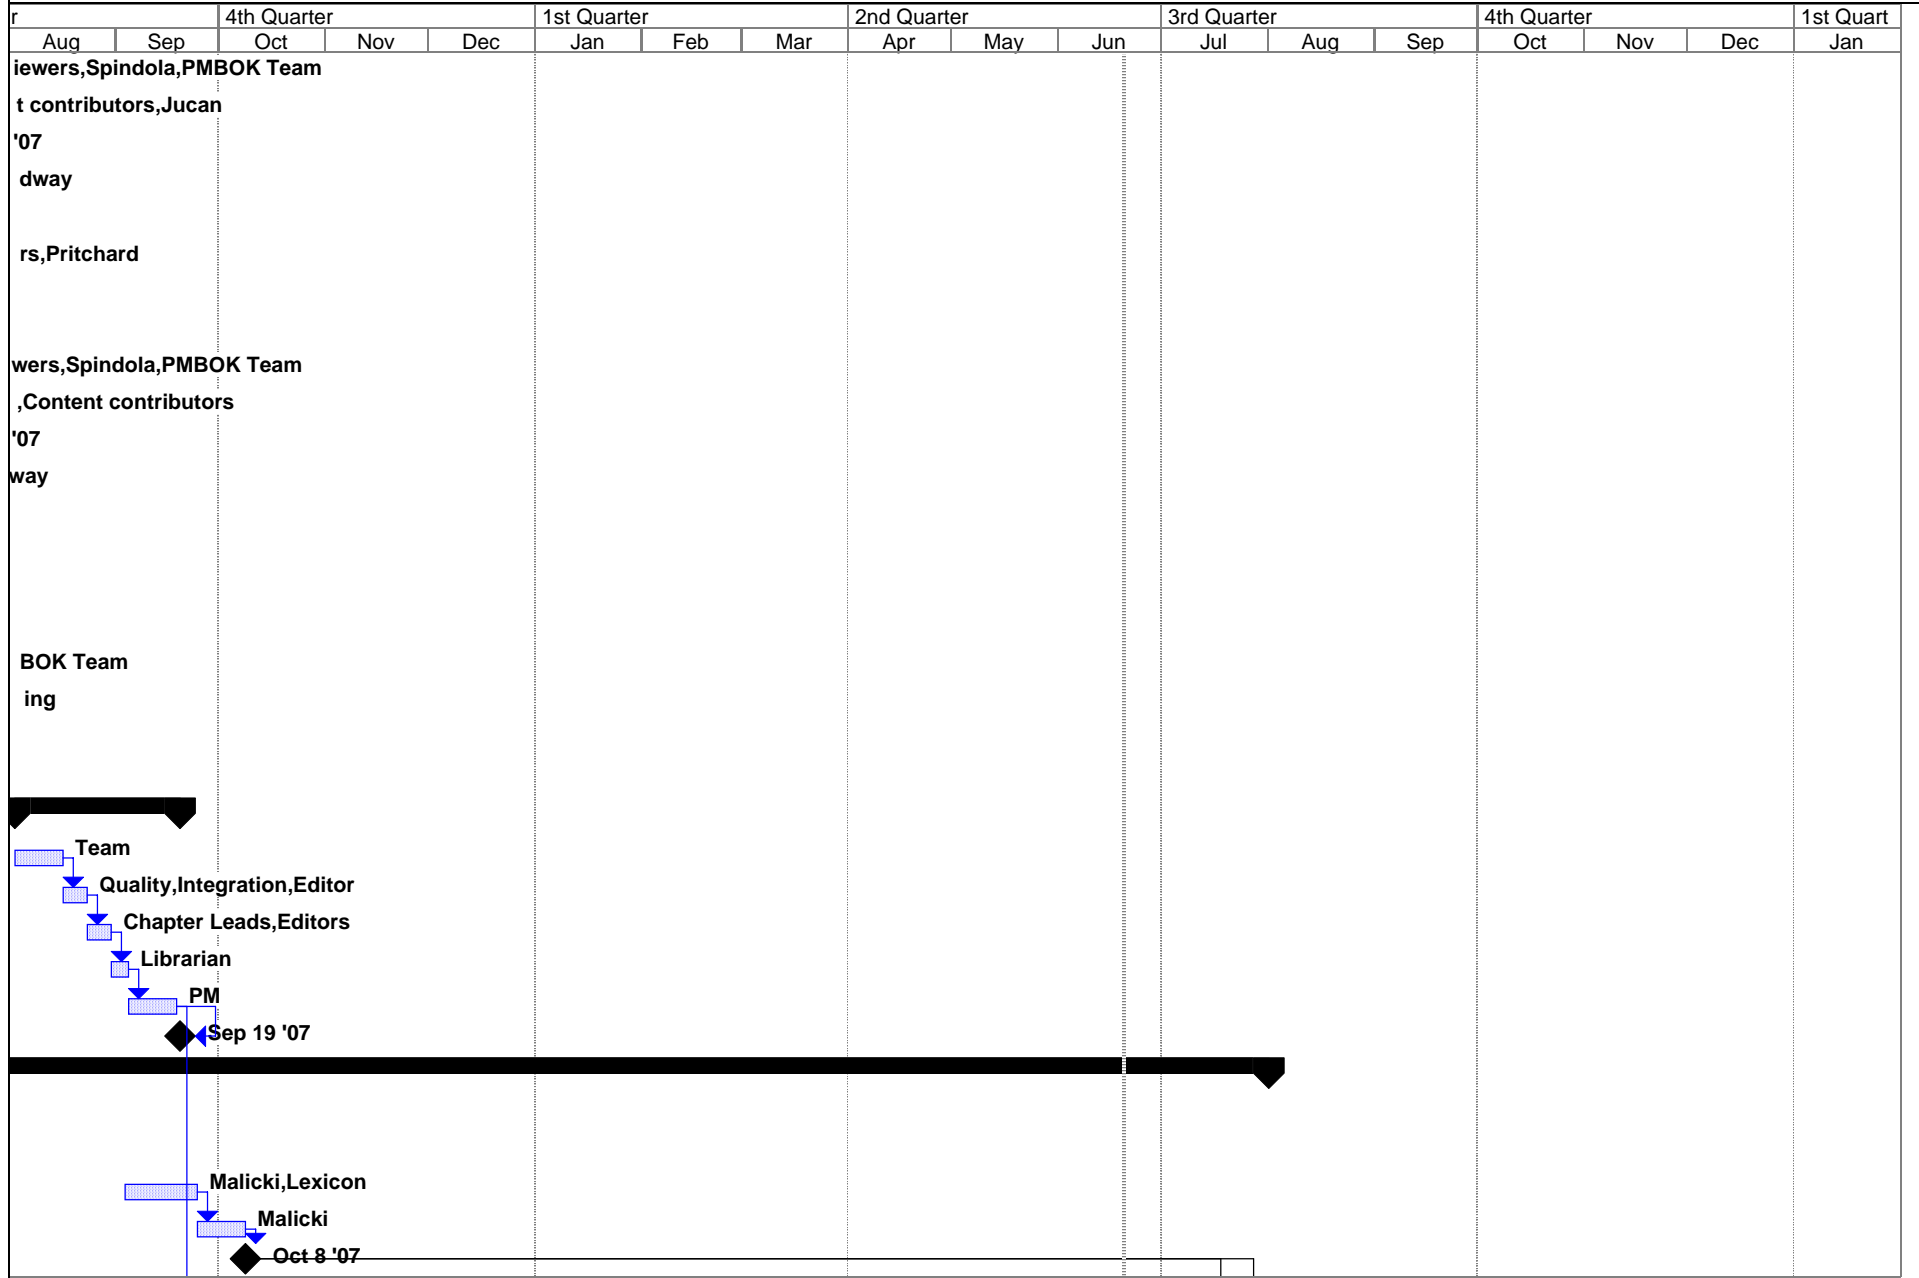

PMBOK Guide - 4th Edition Schedule

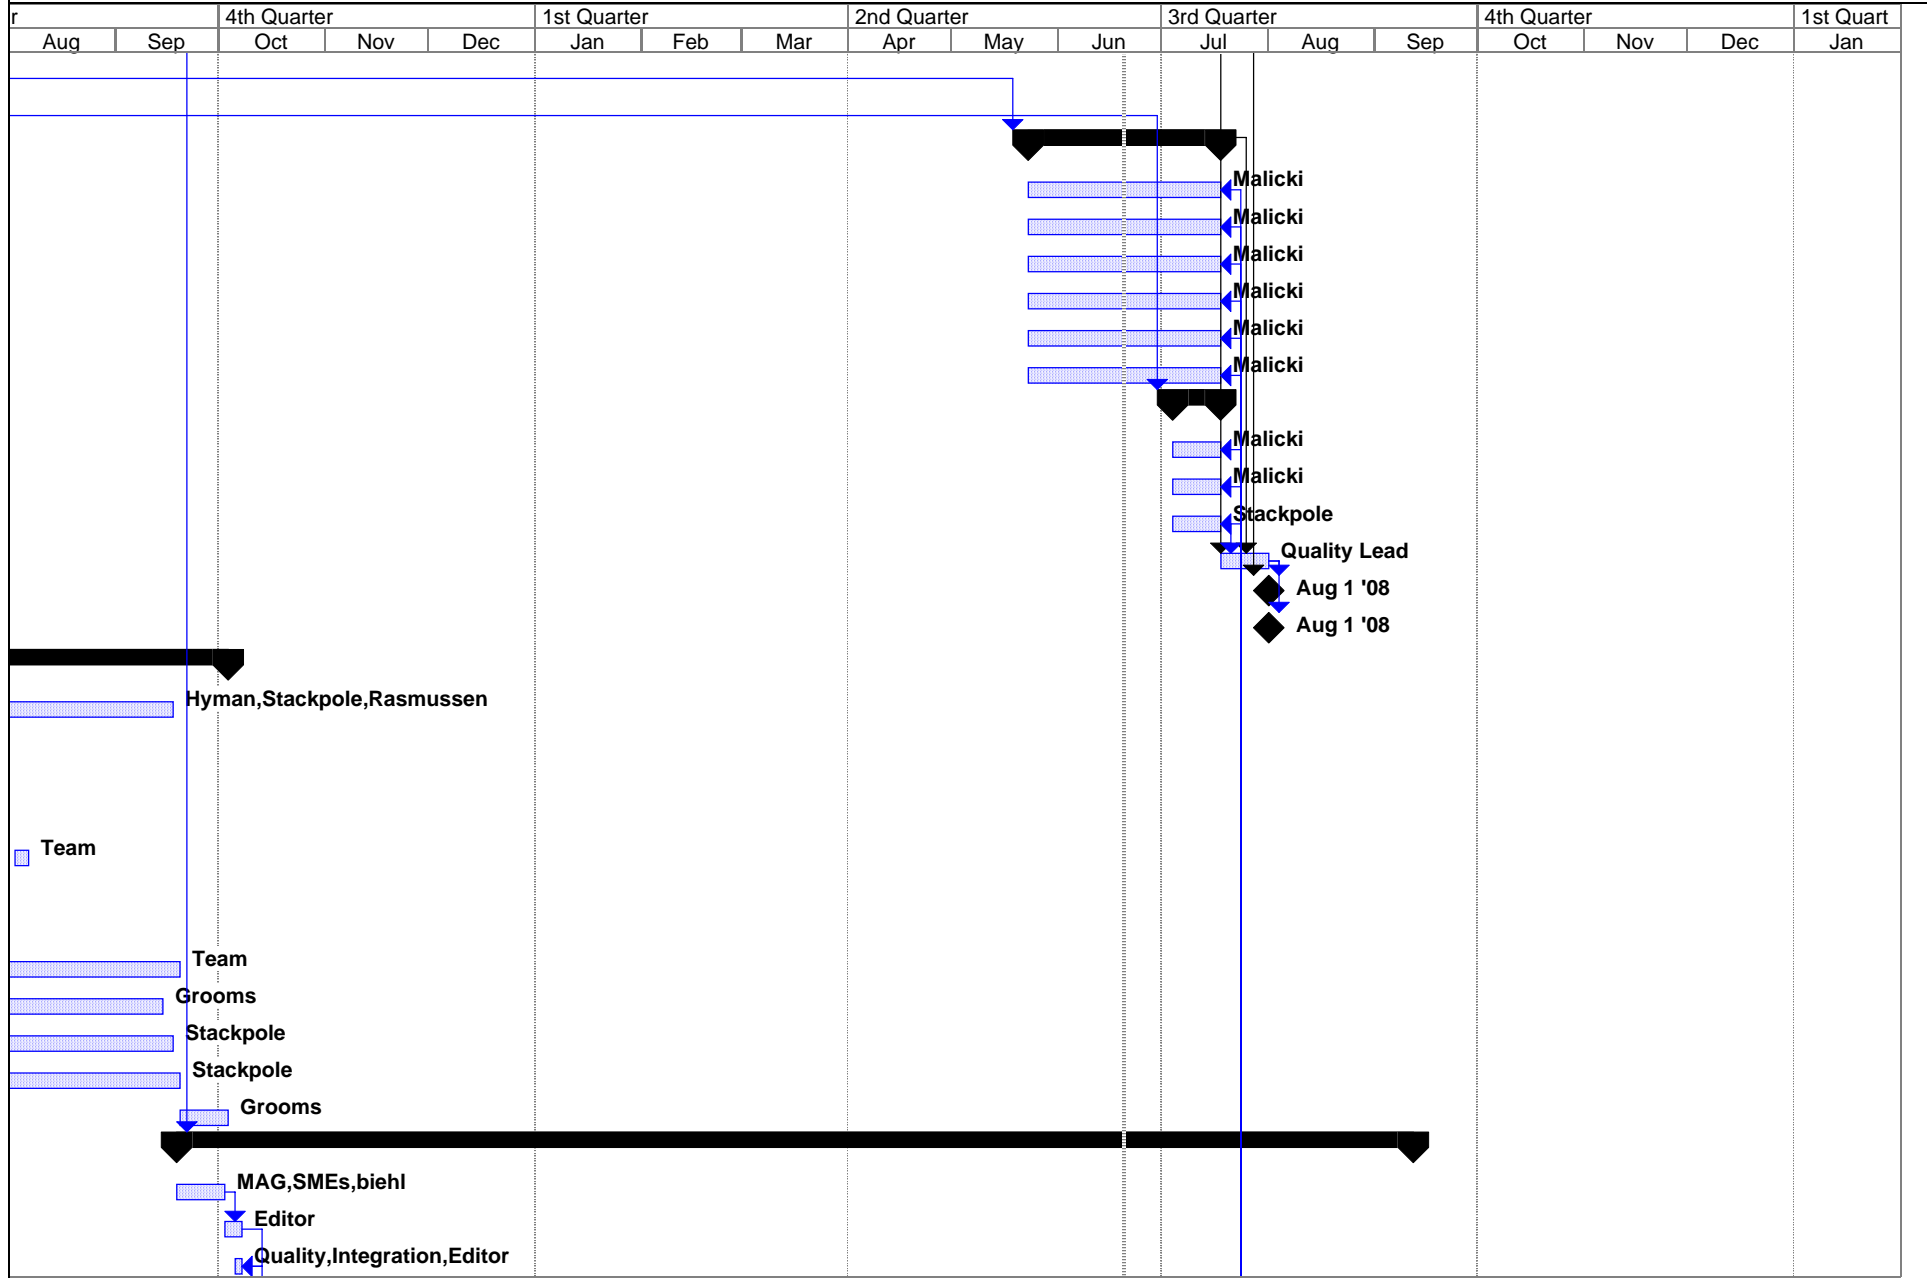

PMBOK Guide - 4th Edition Schedule

